

PHONE: 972-612-3946 FAX: 972-509-2849 PLANO:ROBERT@GMAIL.COM

OFFICE HOURS ARE MONDAY THROUGH FRIDAY 8AM TO 6:30PM AND SATURDAY FROM 9AM TO 2PM

# PROPERTY INSPECTION REPORT

	(Name of Client)	
Concerning:	Lazy Oak, Plano, TX	
	(Address or Other Identification of Inspe	cted Property)
By:	Robert Taylor / 3619	
	(Name and License Number of Inspector)	(Date)

This property inspection report may include an inspection agreement (contract), addenda, and other information related to property conditions. If any item or comment is unclear, you should ask the inspector to clarify the findings. It is important that you carefully read ALL of this information.

This inspection is subject to the rules ("Rules") of the Texas Real Estate Commission ("TREC"), which can be found at www.trec.state.tx.us.

The TREC Standards of Practice (Sections 535.227-535.231 of the Rules) are the minimum standards for inspections by TREC-licensed inspectors. An inspection addresses only those components and conditions that are present, visible, and accessible at the time of the inspection. While there may be other parts, components or systems present, only those items specifically noted as being inspected were inspected. The inspector is not required to move furnishings or stored items. The inspection report may address issues that are code-based or may refer to a particular code; however, this is NOT a code compliance inspection and does NOT verify compliance with manufacturer's installation instructions. The inspection does NOT imply insurability or warrantability of the structure or its components. Although some safety issues may be addressed in this report, this inspection is NOT a safety/code inspection, and the inspector is NOT required to identify all potential hazards.

In this report, the inspector will note which systems and components were Inspected (I), Not Inspected (NI), Not Present (NP), and/or Deficient (D). General deficiencies include inoperability, material distress, water penetration, damage, deterioration, missing parts, and unsuitable installation. Comments may be provided by the inspector whether or not an item is deemed deficient. The inspector is not required to prioritize or emphasize the importance of one deficiency over another.

Some items reported as Deficient may be considered life-safety upgrades to the property. For more information, refer to Texas Real Estate Consumer Notice Concerning Recognized Hazards, form OP-I.

This property inspection is not an exhaustive inspection of the structure, systems, or components. The inspection may not reveal all deficiencies. A real estate inspection helps to reduce some of the risk involved in purchasing a home, but it cannot eliminate these risks, nor can the inspection anticipate future events or changes in performance due to changes in use or occupancy. It is recommended that you obtain as much information as is available about this property, including any seller's disclosures, previous inspection reports, engineering reports, building/remodeling permits, and reports performed for or by relocation companies, municipal inspection departments, lenders, insurers, and appraisers. You should also attempt to determine whether repairs, renovation, remodeling, additions, or other such activities have taken place at this property. It is not the inspector's responsibility to confirm that information obtained from these sources is complete or accurate or that this inspection is consistent with the opinions expressed in previous or future reports.

Items identified in the report do not obligate any party to make repairs or take other action, nor is the purchaser required to request that the seller take any action. When a deficiency is reported, it is the client's responsibility to obtain further evaluations and/or

Report Identification: Lazy Oak, Plano, TX

I=Inspected	NI=Not Inspected	NP=Not Present	D=Deficiency	
I NI NP D	1	Inspection	ı İtem	

cost estimates from qualified service professionals. Any such follow-up should take place prior to the expiration of any time limitations such as option periods. Evaluations by qualified tradesmen may lead to the discovery of additional deficiencies which may involve additional repair costs. Failure to address deficiencies or comments noted in this report may lead to further damage of the structure or systems and add to the original repair costs. The inspector is not required to provide follow-up services to verify that proper repairs have been made.

Property conditions change with time and use. For example, mechanical devices can fail at any time, plumbing gaskets and seals may crack if the appliance or plumbing fixture is not used often, roof leaks can occur at any time regardless of the apparent condition of the roof, and the performance of the structure and the systems may change due to changes in use or occupancy, effects of weather, etc. These changes or repairs made to the structure after the inspection may render information contained herein obsolete or invalid. This report is provided for the specific benefit of the client named above and is based on observations at the time of the inspection. If you did not hire the inspector yourself, reliance on this report may provide incomplete or outdated information. Repairs, professional opinions or additional inspection reports may affect the meaning of the information in this report. It is recommended that you hire a licensed inspector to perform an inspection to meet your specific needs and to provide you with current information concerning this property.

Inspection Time: 9:00 AM	✓ Mechanical & Structural	This Is Your Invoice
<u>Weather</u> : Clear Sky	☐ Pier & Beam	Fee: \$
Temp: Avg. 70 degrees F	☐ WDI (Termite)	Paid By: Check
Realty Co: Keller Williams	Sprinkler	Received:
Agent:	Pool	Robert W. Taylor
Structure Type: Single Family Two Story	☐ Spa	
Status: Vacant, New Home	☑ Gas Line	
Who Is Present: Only the inspector	Outbuilding	
Directional reference the dwelling faces: North	☐ Radon	

NOTE There Are Some Internet Links in the report which will connect to helpful information. 1] must be connected to internet 2] position the cursor over <a href="http://address">http://address</a> and select Control & Click

IMPORTANT - This Report is Not Valid without the signed, separate, <u>3 PAGE VISUAL INSPECTION AGREEMENT</u>. If you did not attend the inspection you will need to email a copy to <u>plano.robert@gmail.com</u> or fax to 972-509-2849. Initial page one and two, sign and date page three. The contract agreement is available at my website <a href="http://aplusinspection.net/agreement.asp">http://aplusinspection.net/agreement.asp</a>

New Helpful Explanation of TREC Report as of February 1st, 2009 http://aplusinspection.net/trec.asp

<u>FONT HIGHLIGHTING</u> IN THE REPORT - **BOLD** an attempt to identify some areas of importance in the report. RED an attempt to flag some important safety issues.

I=Inspected NI=Not Inspected NP=Not Present D=Deficiency
I NI NP D Inspection Item

#### I. STRUCTURAL SYSTEMS

 $\square$   $\square$   $\square$  A. Foundations

Type of Foundation(s): Slab-On-Grade

Comments:

This structure has no visual evidence of any significant movement, shifting or differential settlement at the time of this inspection.

This report does not predict future movements, repair potentials or past repair histories. Conditions covered by floor coverings, furniture, and stored items or hidden underground are unknown.

☑ □ □ ☑ B. Grading & Drainage Comments:

Lower soil to expose at least two inches of foundation and slope to drain away from structure. Do not create a condition where water will pool up against the foundation. Areas of concern include south side of garage and NW corner of entry at base of step.

### ✓ □✓ C. Roof Covering Materials

Type(s) of Roof Covering: Concrete Spanish Tile

Viewed From: Observations made from ground with binoculars because walking on tile can cause damage.

Comments:

Random Sampling of Material Reveals: The tiles were not removed to review how they are fastened


Appears to be in good condition, however possible leak refer to the Section F. Ceilings & Floors. I can see plastic zip ties at the northeast corner of the garage holding tiles in place, not an acceptable method of attachment.

I=Inspected		Lazy Oak, Plano, T <b>NI=Not Inspected</b>	NP=Not Present D=Deficiency
I NI NP	D		Inspection Item
		D. Roof Structur	re & Attic
		Viewed From	n:
			closet access - Entered attic and performed a visual inspection. Observations floored areas. Parts of the attic are not readily accessible.
			Average Depth of Insulation: 11 to 13 inches. Average Thickness of Vertical Insulation: NA
		Comments:	
			viewing limitations, tight niches and angles. Dense insulation and/or low roofs & ducting afe entry beyond decked areas.
			or & Exterior) Comments:
		EXTERIOR	s cement with foam trim at window surrounds, door surrounds and decorative
		appointments as any penet	s. Remember to maintain water tight seals at all window and door frames as well trations through the finish material specifically where foam is used. Keep sprinkler and so they do not spray the home.
团 🗆 🗆	<b>7</b>	E C.22 9 E	
		Stain and cr	oors Comments:  cack in ceiling finish at the game room may be water penetration from the and correct.
		1001, 104104	
	Y	,	or & Exterior) Comments: ad bolt is tight to turn.
			arage advise seal the exterior base of door jamb and along the threshold.
		Strike plate a	adjust at the game room closet.
		Gap betweer	n door and door stop when closed at northwest bedroom.
	$\overline{\checkmark}$	H. Windows Cor	nments:
		to the window	fficult to open at living room 1 (window panel in operable sash is not bonding well w frame (top edge)), and single car garage 1.
			not in place at hall to garage.
		Five screens	stored beneath the stair closet and more in the garage.

Report Identification: Lazy Oak, Plano, TX NI=Not Inspected I=Inspected NP=Not Present **D=Deficiency** I NI NP **Inspection Item Stairways (Interior & Exterior)** *Comments:* J. Fireplace/Chimney Comments: Family Room Fire Box - Type: Is a gas burning appliance, it does not burn wood. A metal firebox with an electric starter which is turned on from a wall switch control. Access to valves are beneath the metal box. K. Porches, Balconies, Decks, and Carports Comments:

Missing a guard rail at the north balcony. Guard rail required where the distance from any

Exterior Balcony:

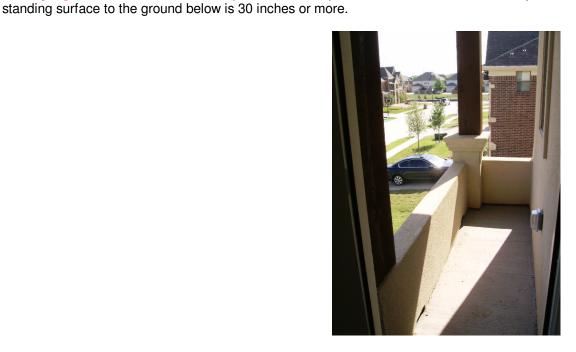

Report Identification: Lazy Oak, Plano, TX I=Inspected NI=Not Inspected NP=Not Present **D=Deficiency** D **Inspection Item** NI NP II. ELECTRICAL SYSTEMS A. Service Entrance and Panels Comments: Service line is Underground / Panel of: Breakers / Main breaker: 200 AMP Location: Garage Arc-Fault Circuit Breakers or Devices - TREC requires that I note the lack of arc-fault circuit breakers per the 2006 electric code in the home serving family rooms, dining, living, parlors, libraries, dens, sunrooms, recreation rooms, closets, hallways, or similar room areas. Note arc-fault breakers are present at bedroom areas.  $M \cup M$ B. Branch Circuits, Connected Devices, and Fixtures Type of Wiring: Copper Comments: Smoke Alarms in the home are inspected by pushing the test button, they are not tested for sensitivity to heat or smoke. Smoke alarms present and working. I Do Not Inspect Heat Sensors connected to the Security Systems. GFCI (ground fault circuit interrupter) TREC requires the comments be based on the 2006 Electric Code. Is missing within 6 feet of the doorway outside of the laundry. OUTLET: game room floor north outlet the screws holding the cover plate do not match and screws are damaged.

SWITCH: No apparent switch function at single car garage one of four switches.

lighting 2. Add rubber gaskets to the landscape lighting sockets to keep water out.

FIXTURE: Non working fixtures (may be bulbs, switches or fixtures) at kitchen 1, landscape

I=Inspected	NI=Not Inspected	NP=Not Present	D=Deficiency	
I NI NP	D	Inspect	ion Item	

### III. HEATING, VENTILATION AND AIR CONDITIONING SYSTEMS

✓ □ □ ✓ A. Heating Equipment

<u>Type</u> Forced Central Air/ <u>Energy Source</u>: Gas *Comments*:

Gas furnaces - limited view of flame and burner compartments (see note below) but the gas furnace operation appears normal.

Note the gas lines are tight against the burner covers making it difficult for a mechanic to access the burner compartment.



V				В.	Cooling	<b>Equipment</b>
---	--	--	--	----	---------	------------------

Type of System: Conventional

Comments:

[Note - temperature differential optimum reading 18 to 20 degrees, 14 & less is deficient.]

<u>Downstairs Zone</u>. Temperature differential [ 19 degrees ]. AC system(s) are operational, suction line cold to touch, differential readings are good.

<u>Upstairs Zone</u>. Temperature differential [ 18 degrees ]. AC system(s) are operational, suction line cold to touch, differential readings are good.

Condensate Drains: Good

Condenser Coil: Good.

Report Identification: Lazy Oak, Plano, TX

I=Inspected	NI=Not Inspe	cted NP=Not Present	D=Deficiency	
I NI NP	D	Ir	spection Item	

## ☑ □ □ ☑ C. Duct System, Chases, and Vents Comments:

Moderately dirty air filters, recommend replacing.

A pleated filter will do a better job of catching airborne particles and keeping the evaporator coil clean.

Downstairs zone the filter cover is bent, one hinge is broken, draws in attic air.



I=Inspected	NI=Not Inspected	NP=Not Present	D=Deficiency	
I NI NP D		Inspection	Item	

#### IV. PLUMBING SYSTEM

#### A. Water Supply System and Fixtures

Location of water meter: between the sidewalk and curb.

Location of main water supply valve: planter north side of single car garage.

Static water pressure reading: water pressure exceeds 80 psi and does not have a pressure regulator, contact plumbing concern. The PSI reading is - 87



Comments:

**Laundry** Dryer Connection Is: Electric

Exterior Faucets - Good.

<u>Kitchen Sink</u> – Sink to granite counter top there are some gaps in the silicone seal which can lead to trapped food particles and encourage mildew.

<u>Laundry Sink</u> – missing aerator at the spout end.

<u>Bathroom Down</u> – Good

<u>Bathroom</u> <u>Master</u> – Good

 I=Inspected
 NI=Not Inspected
 NP=Not Present
 D=Deficiency

 I NI NP D
 Inspection Item

#### Bathroom North Hall Upstairs -

Sink - hot water valve is binding when turning.

**Apparent leak associated with this bathroom.** When running the sink and tub water drips out from behind the stucco at the grade level in the front planter below.





B. Drains, Wastes, and Vents Comments:
See comments water supply systems above regarding upstairs bath leak.
C. Water Heating Equipment  Energy Source: Gas / Capacity: Tankless Water Heater.  Comments:  Mounted to the exterior of the home at the east elevation



Also I could see plastic water line connections at the heating system ask your builder whether the piping in this home is PEX (plastic) or copper tubing.

$ oldsymbol{I} \square \square \square \square oldsymbol{I} oldsymb$	D.	Hydro-Massage Therapy Equipment Comments:
		Spa tub there is no access panel to underside of tub. IRC Code (P2720.1 effective 2003), A door or
		panel of sufficient size shall be installed to provide access to the pump for repair and/or
		replacement. Apparently the present condition is acceptable with the city of Plano.

Report Identification: Lazy Oak, Plano, TX I=Inspected NI=Not Inspected NP=Not Present **D=Deficiency** NI NP D **Inspection Item** V. APPLIANCES A Dishwasher Comments: The lower panel is not removed for inspection. **B.** Food Waste Disposer Comments: C. Range Exhaust Vent Comments: Is ducted to the exterior through side wall. D. Ranges, Cooktops, and Ovens Comments: If present delay timers and self cleaning mode are not tested. Gas Cooktop - good Electric Oven: Upper degrees [na], Lower degrees [370] when set to 350F. Oven registered 20 degrees higher than what it is set for. E. Microwave Oven Comments: Not checked for radiation leaks. Thermometer probes are not tested. Special multifunctional units are operated in the microwave mode only. Door rubbing on the trim kit. F. Trash Compactor Comments: G. Mechanical Exhaust Vents and Bathroom Heaters Comments: **H.** Garage Door Operator(s) Comments: Does not include the operation of remote control. Double car operators Good. Single car operator did not close without holding the control button down. May be the bright sun light affecting the infrared beam (time tested 10 AM in the morning). Beam height should be mounted so that it is 6 inches above the floor. (TREC guidelines and/or per manufacture install specifications).

Is limited to the visible components.

**Doorbell and Chimes** Comments:

J. Dryer Vents Comments:

 I=Inspected
 NI=Not Inspected
 NP=Not Present
 D=Deficiency

 I NI NP D
 Inspection Item

VI.	$\mathbf{O}$	PΊ	П	N	N	Α	ı	[ , !	S	V	S	$\Gamma$	F.	١	1	S	

**☑ ☐ ☐ A.** Lawn and Garden Sprinkler Systems Comments:

Time clocks are operated in the manual mode only.

[Time clock #1]

Stations available 6. Number of stations in use 6.

Stations not mentioned did not require further comment.

Station #2 burried head against the east side of the garage.

There is no rain/freeze guard present to override the sprinkler time clock.

Full coverage surrounding home however adjust for improved coverage at the area near the front door between the walkway and the living room.

Coverage between west sidewalk and fence could be improved.

Valve cover broken at the west yard.



	$\overline{\checkmark}$	В.	Swimming Pools, Spas, Hot Tubs, and Equipment Comments:
		C.	Outbuildings Comments:
		D.	Outdoor Cooking Equipment Comments:
		Е.	Gas Supply Systems Comments:  No measurable movement through gas meter at time of test and no gas odor detected at appliance connections or otherwise.
	V	Н.	Whole-House Vacuum Systems Comments:
	$\overline{\checkmark}$	I.	Other Built-in Appliances Comments:

Report Identification: Lazy Oak, Plano, TX

I=Inspected	NI=Not Inspected	NP=Not Present	D=Deficiency		
I NI NP D	Inspection Item				

#### **OBSERVATIONS**

The following observations about the property, are not considered to be a part of the inspection, but noted for your general information.

#### **GENERAL** -

Recommend to seal all tile grout in home. Kitchen nook light fixture is not hanging level. Single car garage needs cleaning and paint touch up.

#### **EXTERIOR** -

Cable cover box is damaged at the NE corner of the lot.

