

PERMITS/INSP PAYMENT RECPT#: 11109572
TOWN OF AMHERST
TOWN HALL
4 BOLTWOOD AVENUE
AMHERST MA 01002

DATE: 05/12/11 TIME: 12:50 CLERK: mirj DEPT:

PAID BY: AYOTTE, ROSALIND JON PAYMENT METH: CHECK 2084

REFERENCE: 9106

AMT TENDERED:

200.00

CHANGE:

.00

SITE ADDRESS: 525 Station Road

FEES:

HEA058

200.00

TOTAL PAID:

200.00


TITLE 5 INSPECTION

PASSED APP 9106 115204



COLD SPRING ENVIRONMENTAL CONSULTANTS INC.

- - Septic Designs
 - Regulatory Compliance
 - · Recycling and Solid Waste
- - Second Opinions



- · Subsurface Investigations
- · Pollution Remediation
- · LSP on Staff
- Forensic Septic Investigations September 5, 2007

AMHERST Bd. of Health

RE: Septic System Inspection 525 Station Road

On this date, we inspected the installation of a Soil Field) found the Absorption System (S. tank and L. installation to be complete (except for completion of cover material and final fill) and in compliance with our plans and 310 CMR 15.000.

The installer representative from (Karls Excavating) and our inspection noted that the system was built properly, in accordance with the state regulations and our plans. The contractor was requested to have sufficient breakout soil on site and properly cover the system according to our plans and may backfill the system after review by local Health Department representatives.

Sincerely,

Cold Spring Environmental Consultants, Inc.

Alan E. Weiss, M.S., L.S.P.

President

Principal Hydrogeologist

Licensed Site Professional #6442

Registered Sanitarian #933


Cold Spring Environmental 350 Old Enfield Road Belchertown, Ma. 01007

413-323-5957, phone 413-323-4916, fax

AS BUILT ATTACHED:

MASS TO STERED SMITH OF MASS TO LEGE TO SMITH OF MASS TO LEGE TO SMITH OF THE PROPERTY OF THE

AS BUILT

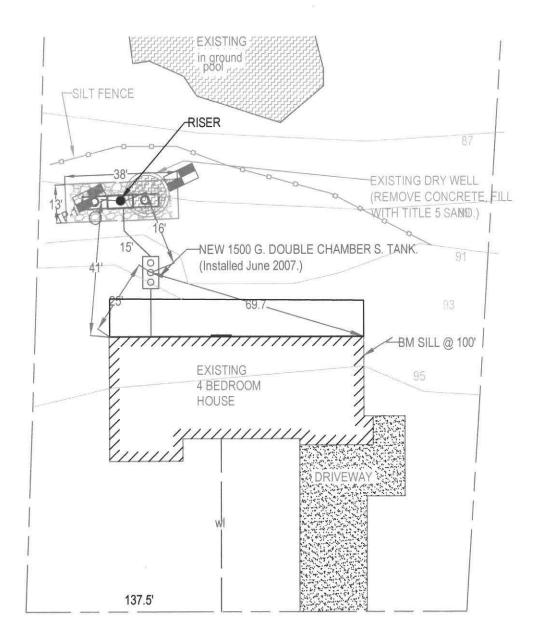

		٠
	*	

SUB-GRADE INSPECTION

Location: 525 Station
Property Owner: Ayo He.
I certify that I have inspected the excavation to sub-grade of the proposed septic system leaching area prior placement of any fill of stone, or construction of any portion of the system.
I further certify that:
 All 'A' and 'B' horizon soils (topsoils and subsoils) were removed in the area of the system. There was no evidence of ground water in the excavation. There was no evidence of "mottles" that would be in conflict with the findings of the deep hole soil profile. That the excavation was accomplished to the proper depth and in conformance with the approved plans.
Designers Name COLD SPRING ENVIRONMENTAL, INC. Street A&50 OLD ENFIELD RD. BELCHERTOWN, MA 01007 Designers Signature Town, State, Zip Code
<u>V13-373-595-7</u> Telephone Number



		4
	ži	
