

## Implementation Status & Results

### Russian Federation

#### Registration Project (P093050)

Operation Name: Registration Project (P093050)		Project Stage: Implementation	Seq.No: 9	Status: ARCHIVED	Last Modified Date: 14-Jun-2011
Country: Russian Federation		Approval FY: 2006			
Product Line: IBRD/IDA	Region: EUROPE AND CENTRAL ASIA		Lending Instrument: Specific Investment Loan		
Implementing Agency(ies): Federal Registration Service					

#### Key Dates

Board Approval Date	13-Jun-2006	Original Closing Date	31-May-2014	Planned Mid Term Review Date	01-Mar-2012	Last Archived ISR Date	06-Nov-2010
Effectiveness Date	23-Apr-2008	Revised Closing Date	31-May-2014	Actual Mid Term Review Date			

#### Project Development Objectives

Project Development Objective (from Project Appraisal Document)

**The new Project Development Objective is to improve the system of registration of legal rights to immovable property by developing standardized, clear and more efficient registration procedures, and by introducing an improved information management system for the registration offices.**

Has the Project Development Objective been changed since Board Approval of the Project?

☒ Yes ☐ No

#### Component(s)

Component Name	Component Cost
Institutional Development of the Registration Service	17.80
Information and Communications Systems	27.40
Improvement of professional skills of registration staff	1.20
Project Management	3.60

#### Overall Ratings

	Previous Rating	Current Rating
Progress towards achievement of PDO	Moderately Satisfactory	Moderately Satisfactory
Overall Implementation Progress (IP)	Unsatisfactory	Moderately Unsatisfactory
Overall Risk Rating		Low

#### Implementation Status Overview

The Registration Project is achieving effective implementation after the institutional reorganization that resulted in the creation of RosReestr. It has initiated procurement of the IT and communication systems for country-wide deployment and is undertaking a number of institutional development tasks to integrate the parts of RosReestr. The May 2011 mission recognized that organizational changes following the unification of registration, cadastre and cartography services, as well as the impact of changes in legislation relevant to the unified system, had constituted the main reasons for delays from the original implementation plan and disbursement schedule. The World Bank acknowledged the prudence of

RosReestr in sequencing the procurement of IT systems after institutional and legal aspects were clarified to ensure efficient use of Loan proceeds. On this basis there was agreement that the current procurement plan represents a realistic calendar and that disbursements will be benchmarked according to its fulfillment. Adherence to the Procurement Plan (and the Action Plan) scheduled is therefore essential for achieving project objectives. There will be continuous dialogue and communications amongst the Bank team, RosReestr and PIU to maintain the momentum.

## Results

### Project Development Objective Indicators

Indicator	Baseline	Current	End Target
Indicator Name Capacity to provide information to clients irrespective of the place of submission of the application and the location of the object (extra-territorial principle of information access)	Value No. of offices with electronic capacity to respond to queries Date 30-Dec-2005 Comment	Value 83 Date 10-Jun-2011 Comment As reported by RosReestr	Value 20 Date 31-May-2014 Comment All Subjects of the Federation - target will be exceeded - using government funds.
Type Custom Indicator	Unit of Measure Text		
Indicator	Baseline	Current	End Target
Indicator Name Client Satisfaction	Value  Date 30-Dec-2005 Comment Not available	Value  Date 10-Jun-2011 Comment Not Available yet	Value  Date 31-May-2014 Comment to be monitored
Type Custom Indicator	Unit of Measure Percentage		

### Intermediate Results Indicators

Indicator	Baseline	Current	End Target
Indicator Name Reduction of time for registration	Value Law stipulates 30 days Date 30-Dec-2005 Comment	Value 30 Date 10-Jun-2011 Comment	Value 15 days in project areas Date 30-Dec-2011 Comment
Type Custom Indicator	Unit of Measure Text		

Indicator		Baseline	Current	End Target
Indicator Name		Value	Value	Value
Submission to Government of a set of normative acts for introduction of electronic archiving and electronic signature of documents		No	Yes	Submitted
		Date	Date	Date
		30-Dec-2005	10-Jun-2011	31-May-2014
Type	Unit of Measure	Comment	Comment	Comment
Custom Indicator	Text		As reported by RosReestr. e-archiving agreed with Government	
Indicator		Baseline	Current	End Target
Indicator Name		Value	Value	Value
Increase of archive capacity (files per m2)		Actual Data for CY 2005 Not available		To be monitored
		Date	Date	Date
		30-Dec-2005	10-Jun-2011	31-May-2014
Type	Unit of Measure	Comment	Comment	Comment
Custom Indicator	Text		target will be determined during preparation of archive strategy, depending on extent of e-archiving usage and financing available.	
Indicator		Baseline	Current	End Target
Indicator Name		Value	Value	Value
Increase in the percentage of surveyed population that understands the requirements and procedures for registration		Not available	Not available	To be monitored
		Date	Date	Date
		30-Dec-2005	13-Jun-2011	31-May-2014
Type	Unit of Measure	Comment	Comment	Comment
Custom Indicator	Text			
Indicator		Baseline	Current	End Target
Indicator Name		Value	Value	Value
Increase in labor productivity (number of registrations performed by one staff in one year)		700	Not available	1200
		Date	Date	Date
		30-Dec-2005	13-Jun-2011	31-May-2014
Type	Unit of Measure	Comment	Comment	Comment
Custom Indicator	Text			

Indicator		Baseline	Current	End Target
Indicator Name		Value	Value	Value
Reduction in time for processing information requests from individuals		7 days	1-7 days depending on office	1 day
		Date	Date	Date
		30-Dec-2005	13-Jun-2011	31-Dec-2011
Type		Unit of Measure	Comment	Comment
Custom Indicator		Text		
Indicator		Baseline	Current	End Target
Indicator Name		Value	Value	Value
Technical capacity to receive and transmit information between Registration and other Federal Agencies, including Cadastre Offices		Number/percent of offices using electronic query technology	83 regional offices (2 percent)	80 percent
		Date	Date	Date
		30-Dec-2005	13-Jun-2011	31-May-2014
Type		Unit of Measure	Comment	Comment
Custom Indicator		Text	As reported by RosReestr	All RF subjects of the Federation
Indicator		Baseline	Current	End Target
Indicator Name		Value	Value	Value
Increase in information requests		Number of website hits/year	8,000 informaiton requests per day	To be monitored
		Date	Date	Date
		30-Dec-2005	13-Jun-2011	31-May-2014
Type		Unit of Measure	Comment	Comment
Custom Indicator		Text		
Indicator		Baseline	Current	End Target
Indicator Name		Value	Value	Value
Increase in percentage of surveyed applicants that are satisfied with the work of the registration offices.		Initial impact assessment		YR6 - 20% increase
		Date	Date	Date
		30-Dec-2005	13-Jun-2011	31-May-2014
Type		Unit of Measure	Comment	Comment
Custom Indicator		Text	Survey planned for 2011-2012	

Indicator		Baseline	Current	End Target
Indicator Name		Value	Value	Value
Number of RosReestr Staff trained using single window technology		0.00		
		Date	Date	Date
		31-Dec-2005	13-Jun-2011	31-May-2014
Type	Unit of Measure	Comment	Comment	Comment
Custom Indicator	Number		Not yet available	to be monitored

### Data on Financial Performance (as of 24-Feb-2011)


#### Financial Agreement(s) Key Dates

Project	Loan No.	Status	Approval Date	Signing Date	Effectiveness Date	Closing Date
P093050	IBRD-48260	Effective	13-Jun-2006	14-Sep-2007	23-Apr-2008	31-May-2014

#### Disbursements (in Millions)

Project	Loan No.	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P093050	IBRD-48260	Effective	USD	50.00	50.00	0.00	0.94	49.06	2.00

### Disbursement Graph

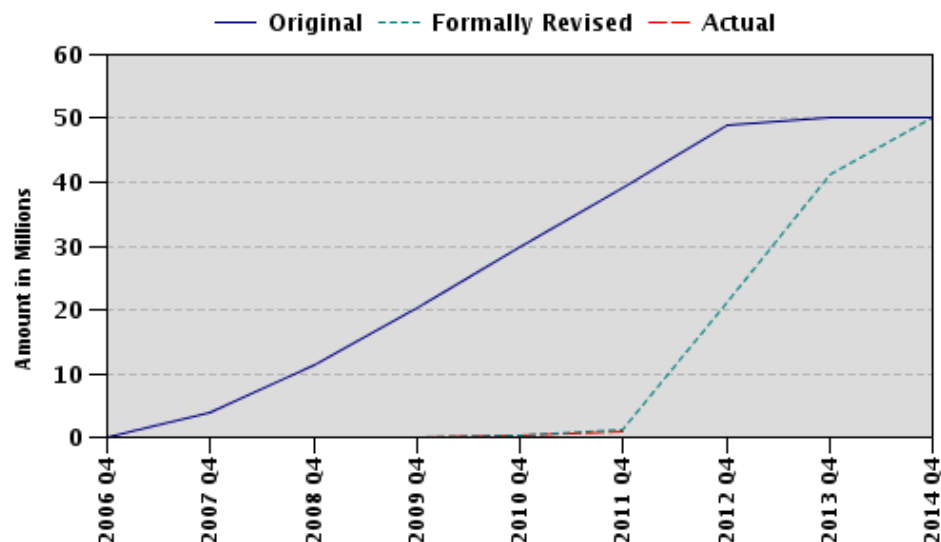

### Key Decisions Regarding Implementation

None

---

### **Restructuring History**

Level one Approved on 23-Aug-2010

---

### **Related Projects**
